BRUHAT BENGALURU

Clients Name	:	Executive Engineer Byatarayanapura Division	
Project Name	:	PACKAGE-9, (Includes 2 Works of Rs 200.00 lakhs) 1) IMPROVEMENTS TO ROADS AND DRAINS AT SINGAPURA, SINGAPURA TEACHERS LAYOUT, RAGHAVENDRA COLONY, BALAJI LAYOUT, SHRINIDHI LAYOUT, VAISNAVI LAYOUT, SAI GARDE	
Project Start Date	:	03-11-18	
Project End Date	:	03-03-19	
Project Length in Months	:	4 Months	

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Earthwork in surface excavation in ordinary soil for leveling and lowering the ground manually (other than foundation of buildings, culverts, roads drains and trenches of pipe line and cables) and removing the excavated stuff to a distance	Cum	599.53	599.53	100	05-11-18	04-11-20	730
3	Removing and refixing stone slabs of drains and pointing in CM (1:3) as per the directions of the Engineer-in-charge of the work .	Sqm	130.41	130.41	100	19-11-18	18-11-20	730
4	Providing granite slabs of selected quality roughly dressed havinf a size of 7.5 cms thick and fixed in cement mortar (1:6) including fixing curing ete., complete as per the directions of the Engineer-in-charge of the work .	Sqm	21.74	21.74	100	03-12-18	22-11-20	720
7	Excavation in Soil using Hydraulic Excavator CK 90 and Tippers with Disposal KSRRB M300-14. Excavation for roadwork in soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and loading in tippers, trimming bottom and side slopes, in	Cum	226.16	226.16	100	31-12-18	30-11-20	700
8	Lead for disposal of earth shall be payable at Carriage rates (Lead & Lift) by mechanical means including loading and unloading and as per the directions of the Engineer-in-charge of the work .	Cum	825.69	825.69	100	05-11-18	01-12-20	757
9	Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement Table 300- 2 complete as per specifications.(Including cost of gravel /	Cum	545.73	545.73	100	05-01-19	15-12-20	710
10	Compaction of original ground with maximum of 6 passes of 8 to 10 tonnes power roller including filling in depression occuring during rolling including cost of all labour, HOM of machinery complete as per specifications and as per the directions of the Engineer-in-charge	Cum	5438.11	5438.11	100	20-01-19	09-01-21	720
11	Providing,laying, spreading and compacting crushed stone aggregates of granite/trap/ basalt to wet mix macadam specification including pre mixing the Material with water at OMC in mechanical	Cum	1476.45	1476.45	100	06-02-19	22-02-21	747
12	Scarifying bituminous course 50mm to 75mm thick along with premix carpet / surface dressing by manual means without disturbing the base and stacking of the debris materials including cost of all labour	Sqm	5438.11	5438.11	100	31-12-18	30-11-20	700
13	Cleaning the existing WBM Road surface including removing of binding materials and other foreign matter with wire brushes and small picks sweeping with brooms or soft brushes and finally dusting with old gunny	Sqm	630.22	630.22	100	21-02-19	02-03-21	740
14	Providing and applying tack coat using 80/100 grade bitumen (VG 10) on granular base such as WBM surface hot bitumen primed at 4kg per 10 sqm heating bitumen in boiler with spray set (Excluding cleaning of Road surface) inlcuding cost of all materials, labhour, HOM of machineries complete as per specifications	Sqm	3741.56	3741.56	100	05-03-19	04-03-21	730
15	Providing and laying bituminous macadam on prepared surface with crushed coarse as per design mix formula for base / binding courseincluding loading of aggregates with F.E. loader, hot mixing of stone aggregates and bitumen in hot mix plant,transporting the	Cum	187.08	187.08	100	05-03-19	04-03-21	730
16	Cleaning the existing black topped surface with brooms,soft brushes and finally dusting with old gunny bags and/or compressed air to receive bituminous treatment including cost of all materials,labhour, HOM of machineries	Sqm	26216.70	26216.70	100	04-04-19	04-03-21	700

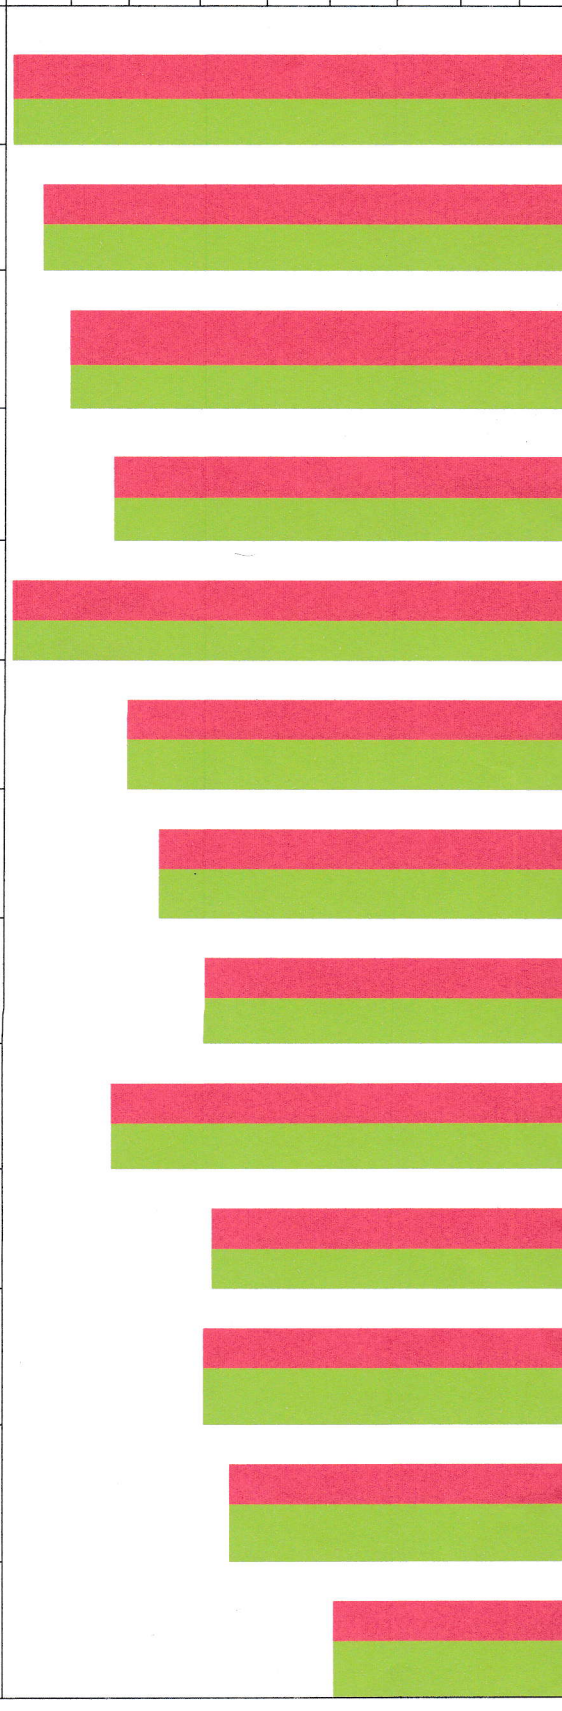

U MAHANAGARA PALIKE

URA GARDEN, VALMIKI NAGARA, ASHERAYA LAYOUT, KUVEMPUNAGARA & NAIDU LAYOUT IN WARD NO. 11 KUVEMPUNAGARA. 2) IMPROVEMENTS TO ROADS AND DRAINS AT RDEN, M S PALYA, BHARATH NAGARA, CHINNASWAMY LAYOUT, MARUTHI LAYOUT, VINAYAKA NAGAR, SINGAPURA PARADISE, IN WARD NO. 11 KUVEMPUNAGARA.

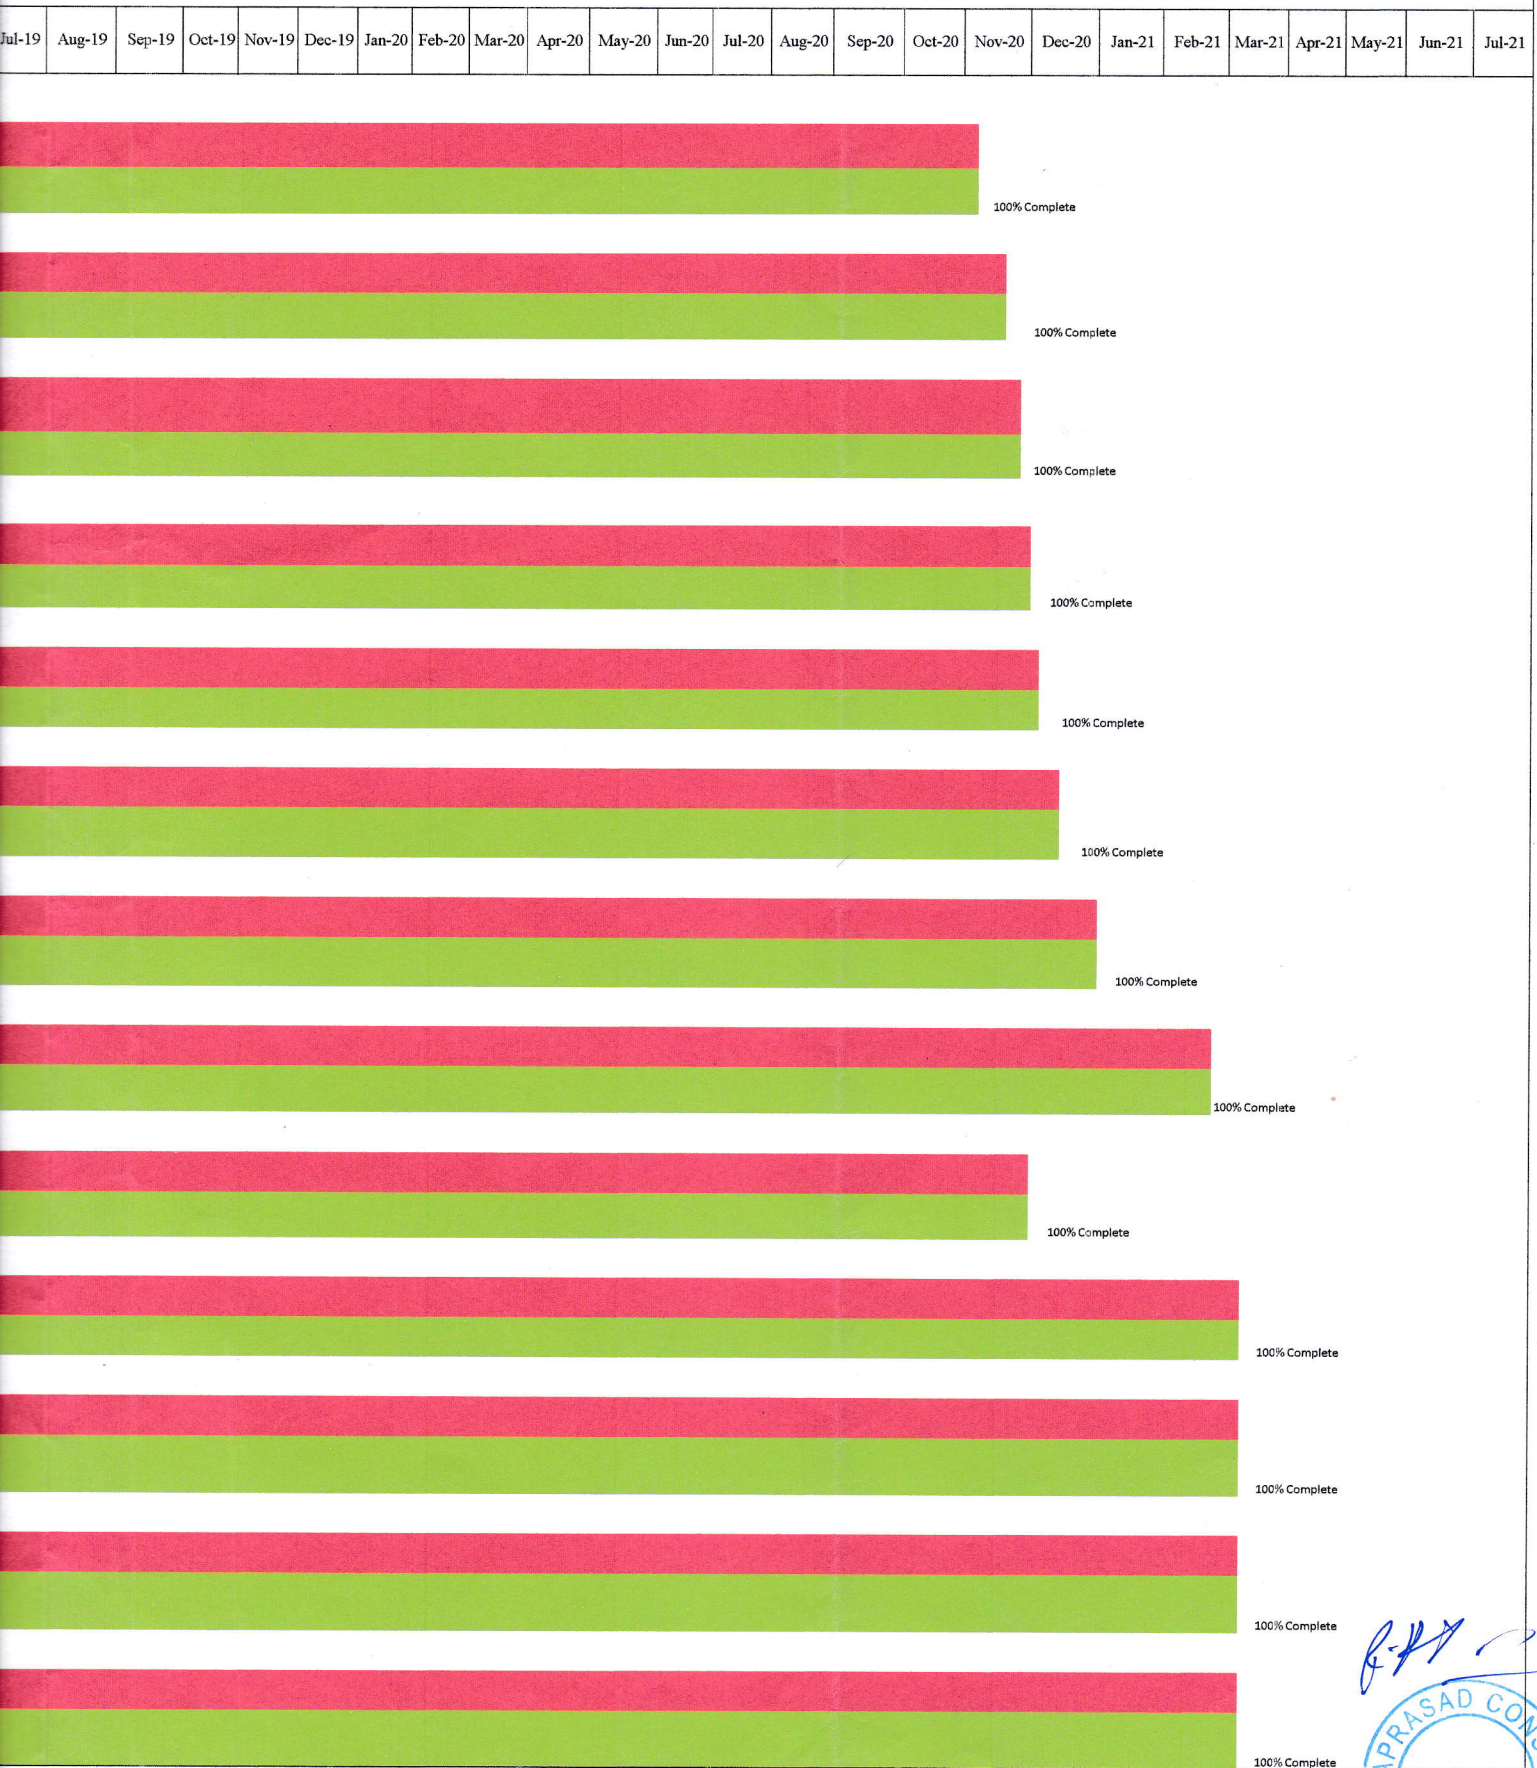

RUDRAPRASAD CONSULTANTS BANGALORE

BRUHAT BENGALURU M

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	PACKAGE-9, (Includes 2 Works of Rs 200.00 lakhs) 1) IMPROVEMENTS TO ROADS AND DRAINS AT SINGAPURA, SINGAPURA G TEACHERS LAYOUT, RAGHAVENDRA COLONY, BALAJI LAYOUT, SHRINIDHI LAYOUT, VAISNAVI LAYOUT, SAI GARDEN,
	Project Start Date	:	03-11-18
	Project End Date	:	03-03-19
	Project Length in Months	:	4 Months

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
17	Providing and applying tack coat using 80/100 grade bitumen(VG10) in boiler fitted with spray set distributor at the rate of 0.20kg per sqm on the existing prepared bituminous surface cleaned with mechanical broom. complete as per specification.	Sqm	26216.70	26216.70	100	24-04-19	11-06-21	779
18	Providing and laying bituminous concrete using crushed aggregates of specified grading,premixed with bituminous binder and filler,transporting the hot mix to work site,laying with a paver finisher to the required grade, level and alignment,rolling	Cum	1048.67	104867.00	10000	24-04-19	11-06-21	779
19	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface:- Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms	Sqm	517.96	517.96	100	14-05-19	17-06-21	765
E1	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site,	Sqm	1158.58	1158.58	100	25-01-19	03-02-21	740

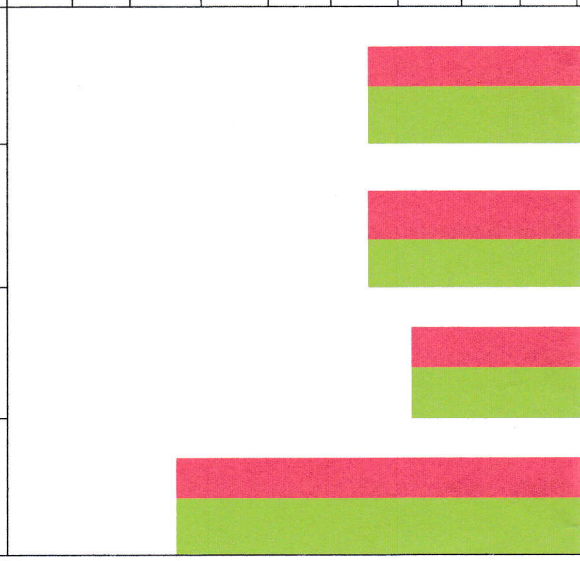

LEGEND

= Planned %

= Executed %

RU MAHANAGARA PALIKE

PURA GARDEN, VALMIKI NAGARA, ASHERAYA LAYOUT, KUVEMPUNAGARA & NAIDU LAYOUT IN WARD NO. 11 KUVEMPUNAGARA. 2) IMPROVEMENTS TO ROADS AND DRAINS AT ARDEN, M S PALYA, BHARATH NAGARA, CHINNASWAMY LAYOUT, MARUTHI LAYOUT, VINAYAKA NAGAR, SINGAPURA PARADISE, IN WARD NO. 11 KUVEMPUNAGARA.

RUDRAPRASAD CONSULTANTS
BANGALORE
